

Project Plan

CBC-BSWA

Industry Partner	CBC
Primary Instructor	Anjana Shah
Team Member	Andrew Sas
Team Member	Oskar Molenda
Team Member	Riley Thomas
Team Member	Shaffaq Hai

Document Revision History

Revision #	Date
0.1	26/09/2025

Table of Contents

1. Executive Summary	3
2. Project Approvers, Reviews and Distribution List.....	3
3. Scope.....	4
4. Deliverables	5
5. Assumptions.....	5
6. Dependencies	5
7. Risk Management	6
8. Communication	7
9. Task Listing (WBS- Work Breakdown Structure).....	8
10. Gantt Chart	9
11. Milestones	9
12. RAM – Responsibility Assignment Matrix.....	10
13. Approval	11

1. Executive Summary

Objective	The objective of this project is to address a repeating problem involving the formatting and manipulation of data for special broadcasts such as the Olympics. This project seeks to fill the current lack of a digital solution, and aims to streamline the currently unintuitive processes for editing existing schedules, and resolving time slot conflicts.
Corporate Goals Addressed	Reduce technician workload and time spent scheduling Olympics manually by using a web application that will format raw data.
Planned Start Date	September 17, 2025
Planned End Date	March 25, 2026

2. Project Approvers, Reviews and Distribution List

Project Role	Name	E-mail	Date
Project Lead	Riley Thomas	riley.thomas@georgebrown.ca	
Lead Engineer	Andrew Sas	andrew.sas@georgebrown.ca	
Engineer	Shaffaq Hai	101500534@georgebrown.ca	
Engineer	Oskar Molenda	101460691@georgebrown.ca	

3. Scope

In Scope	Out of Scope
Users will be able to upload schedule data, Fix schedule conflicts and overlapping timeslots	Formatted Data will directly feed into the CBC backend
Users will be able to View, Edit, Save, Retrieve formatted or unformatted data	Maintenance and Support for the project will not persist past the project end-date
Users will be able to use a Web-Based platform to complete their task	

4. Deliverables

Deliverable	Description
Project Progress Plan	Outlines the timeline and stages of project execution.
Web Prototype	An initial, minimal design to allow for testing and feedback
Web Application Deployment	Final product is deployed

5. Assumptions

This project makes the following assumptions:

- The raw XLSX data that the application will receive is formatted in a standardized manner.
- The application will be beneficial to stakeholders
- No internal or external team is currently working with the stakeholders to solve this problem

6. Dependencies

Dependency	Internal / External	Dependency Type
Front End	Internal	Finish-to-Finish
Database	Internal	Start-To-Start
Load Balancing Algorithm	Internal	Start-To-Start
Time Conflict Flagging	Internal	Finish-to-Finish
Importing Data	Internal	Start-To-Finish
Exporting Data	Internal	Finish-to-Finish
Third Party Media Program Data	External	Finish-to-Finish

7. Risk Management

Potential Risk	Severity (H/M/L)	Likelihood (H/M/L)	Management Strategy
CBC Develops the app themselves	H	L	Our team will provide more features than that is potentially manageable by CBC technicians themselves.
Other Scheduling Applications services may compete	L	L	Our team will have less overhead cost compared to the competition

8. Communication

Reporting

Report	Audience	Frequency
Project Progress Report	CBC, Anjana	Once every 3 months
Self Progress Report	Team-members	Once every 2 months


Meetings

Meeting	Purpose	Attendees	Frequency
Weekly Standup	Track project progress / establish goals	All Members	Weekly
Discord Server	Regular off-site communication	All Members	Messages will be sent / responded to as necessary

9. Task Listing (WBS - Work Breakdown Structure)

Reference	Tasks	Duration	Dependency
A	Gather Project Requirements From Stakeholders	2 Weeks	-
B	Create Design Document	2 Weeks	A
C	Create Wireframes	1 Week	B
D	Design Conceptual / Logical data models	2 Weeks	C
E	Finalize Technical Stack and Tools	1 Day	-
F	Design UI Mockups	1 Week	C
G	Create UI Prototype	2 Weeks	F
H	Design App Database	1 Week	D
I	Build App Backend	2 Weeks	H
J	Build App Frontend	4 Weeks	G
K	Integrate App Database	3 Days	I
L	Testing and Debugging	3 Days	K
M	Fix Issues Found During Testing	3 Days	L
N	Deploy Prototype	1 Day	M
O	Receive feedback from CBC	3 Days	N
P	Refine Product based on feedback	1 Week	O
Q	Deploy MVP	2 Days	P
R	Present Finalized Product	2 Days	Q

10. Gantt Chart

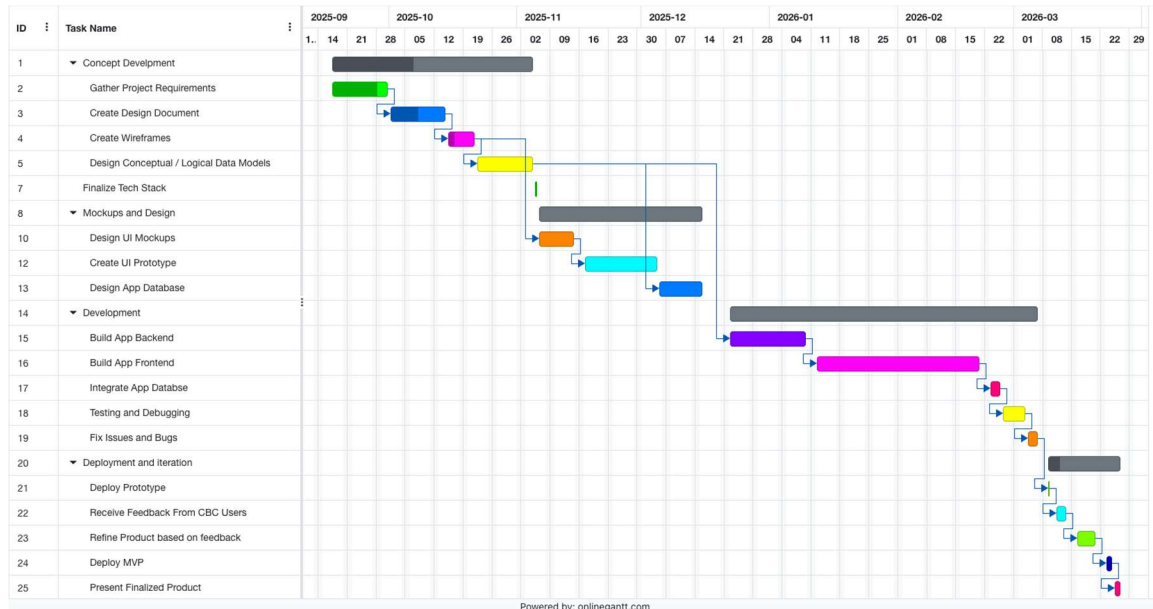

11. Milestones

Major Activity or Milestone	Estimated Milestone Target date	Owner/Reviewer Team Members
Create Project Design Documents	Oct 2025	
Finalize Technical Stack & Tools	Nov 5 2025	
Finalize UI Design	Nov 19 2025	
Create App UI Prototype	Dec 3 2025	
Finalize Back End	Jan 19 2026	

Integrate App Database	Feb 20 2026	
Finalize Front End	March 3 2026	
MVP Testing and Debugging	March 9 2026	
Deploy MVP	March 26 2026	
Present Finalized Product	March 30 2026	

12. RAM – Responsibility Assignment Matrix

Task	Riley Thomas	Andrew Sas	Shaffaq Hai	Oskar Molenda
Establish Project Requirements	S	P	S	S
Design Project Functionality	P	S	S	S
Design Graphical Interface	P	S	S	S
Back End Functionality	S	P	S	S
Testing	S	S	P	S

13. Approval

The signatures below indicate their approval of the contents of this document.

Project Role	Name	Signature	Date
Project Lead	Riley Thomas	Riley Sas	2025-07-25
Lead Engineer	Andrew Sas	Andrew Sas	2025-07-25
Engineer	Shaffaq Hai	Shaffaq Hai	2025-07-25
Engineer	Oskar Molenda	Oskar Molenda	2025-07-25
